





North Augusta High School Athletics Complex

EXECUTIVE SUMMARY REPORT MAY 2025

NORTH AUGUSTA HIGH SCHOOL ATHLETICS COMPLEX

ACTIVITIES CURRENTLY UNDERWAY:

- Batting Building
- Food Service Equipment
- Lockers
- Sod
- Batter's Eye

ACTIVITIES COMPLETE:

- Dugout Footings
- Under Slab
- Slabs Poured
- Light Poles
- Roofing
- Sewer
- Seating
- Storm Drainage
- Electrical
- Curb and Gutter
- Score Boards
- Painting
- Road Work
- Flooring

PROJECT SCHEDULE:

Substantial Completion Date, Scheduled: May 1, 2025

PROJECT BUDGET:


Original Contract Sum:	\$ 7,381,428.00
Net Change by Change Order:	\$ 437,241.00
Contract Sum to Date, Building & Site:	\$ 7,818,669.00
Amount Paid to Date, Building & Site:	\$5,331,729.71

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH

There have been no requests for change order approved this month.





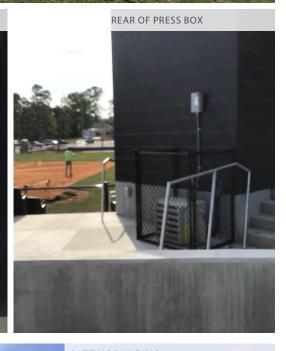

COMPLEX ENTRANCE



