BOARD AGENDA ITEM

November 10, 2026

SUBJECT:

Construction status report for the North Augusta High Auditorium addition and renovation project

BACKGROUND INFORMATION:

In an effort to keep the board current on the status and budget of this school construction project, the architects for this project, McMillan Pazdan Smith (MPS) and the administration prepare a bi-monthly status report for the board's review.

ADMINISTRATIVE CONSIDERATION:

A construction status report for the board is attached for review from McMillan Pazdan Smith (MPS).

RECOMMENDATIONS:

Review and accept the status information as indicated on the report.

ATTACHMENT:

North Augusta High Auditorium addition and renovation project executive summary report

PREPARED BY:

Tim Yarborough
Michael F. Jara



AIKEN COUNTY

PUBLIC SCHOOLS

EXECUTIVE SUMMARY REPORT

NORTH AUGUSTA HIGH SCHOOL AUDITORIUM RENOVATION

AIKEN COUNTY PUBLIC SCHOOL DISTRICT

NOVEMBER 2026

AIKEN COUNTY PUBLIC SCHOOLS

H.G. REYNOLDS COMPANY, INC.

mcmillan pazdan smith ARCHITECTURE

NORTH AUGUSTA HIGH SCHOOL
AUDITORIUM RENOVATION

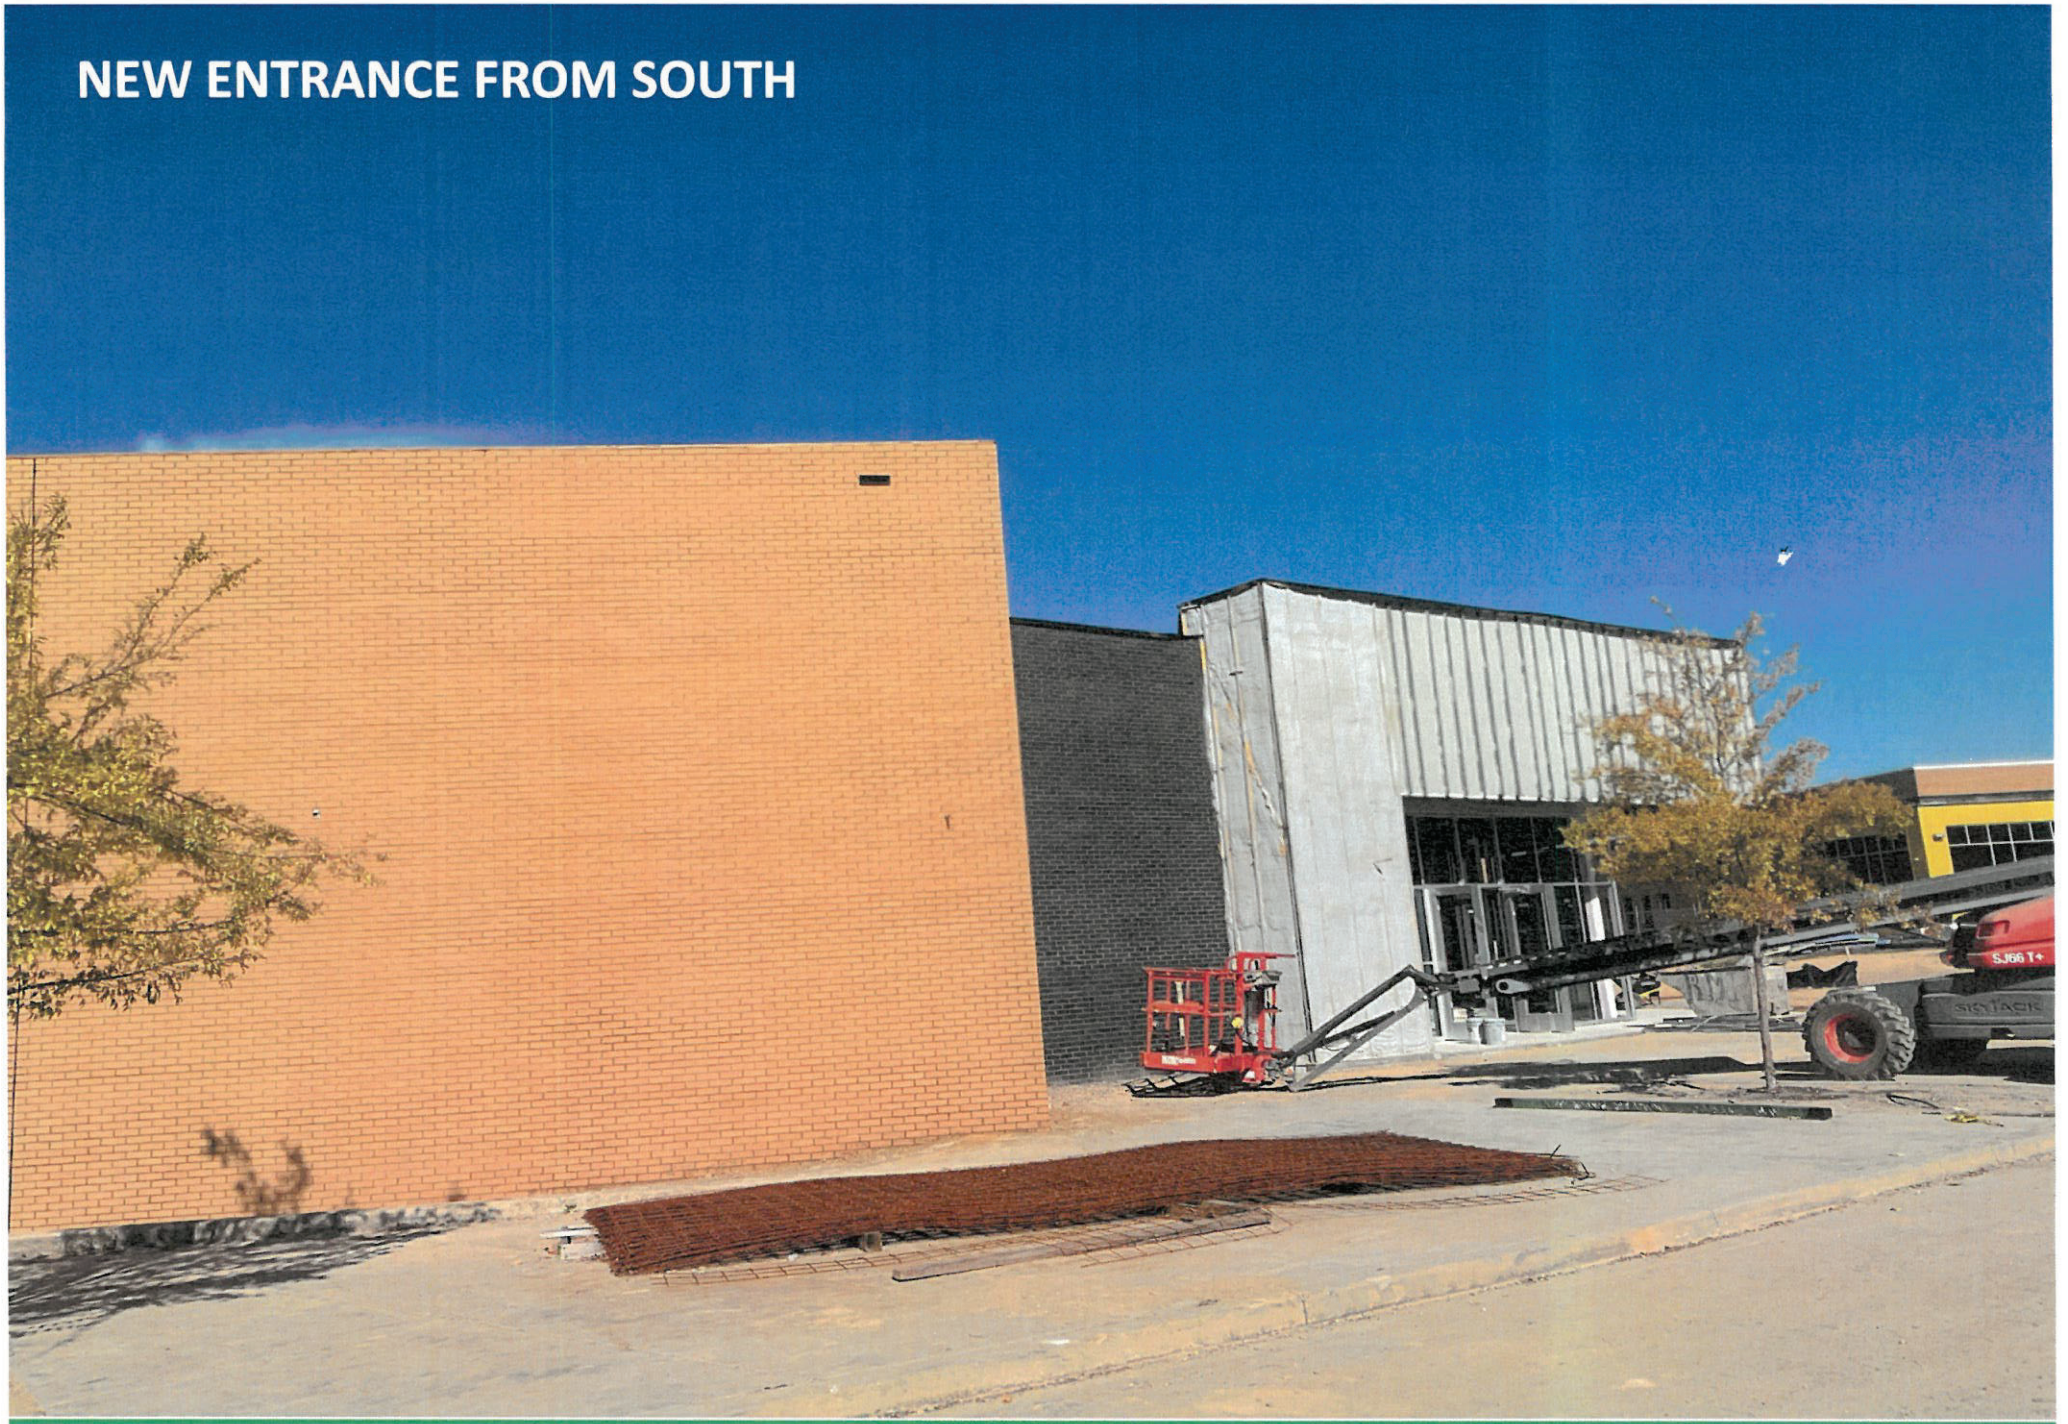
CURRENT AND UPCOMING ACTIVITIES:

- Electrical
- Plumbing
- Sheetrock
- Storefront
- Painting
- Seat Risers

ACTIVITIES COMPLETE:

- Acoustical Clouds
- CMU
- Structural Steel
- Transformer
- HVAC
- Concrete Slabs
- Roofing

NEW ENTRANCE FROM SOUTH



AIKEN COUNTY PUBLIC SCHOOL DISTRICT

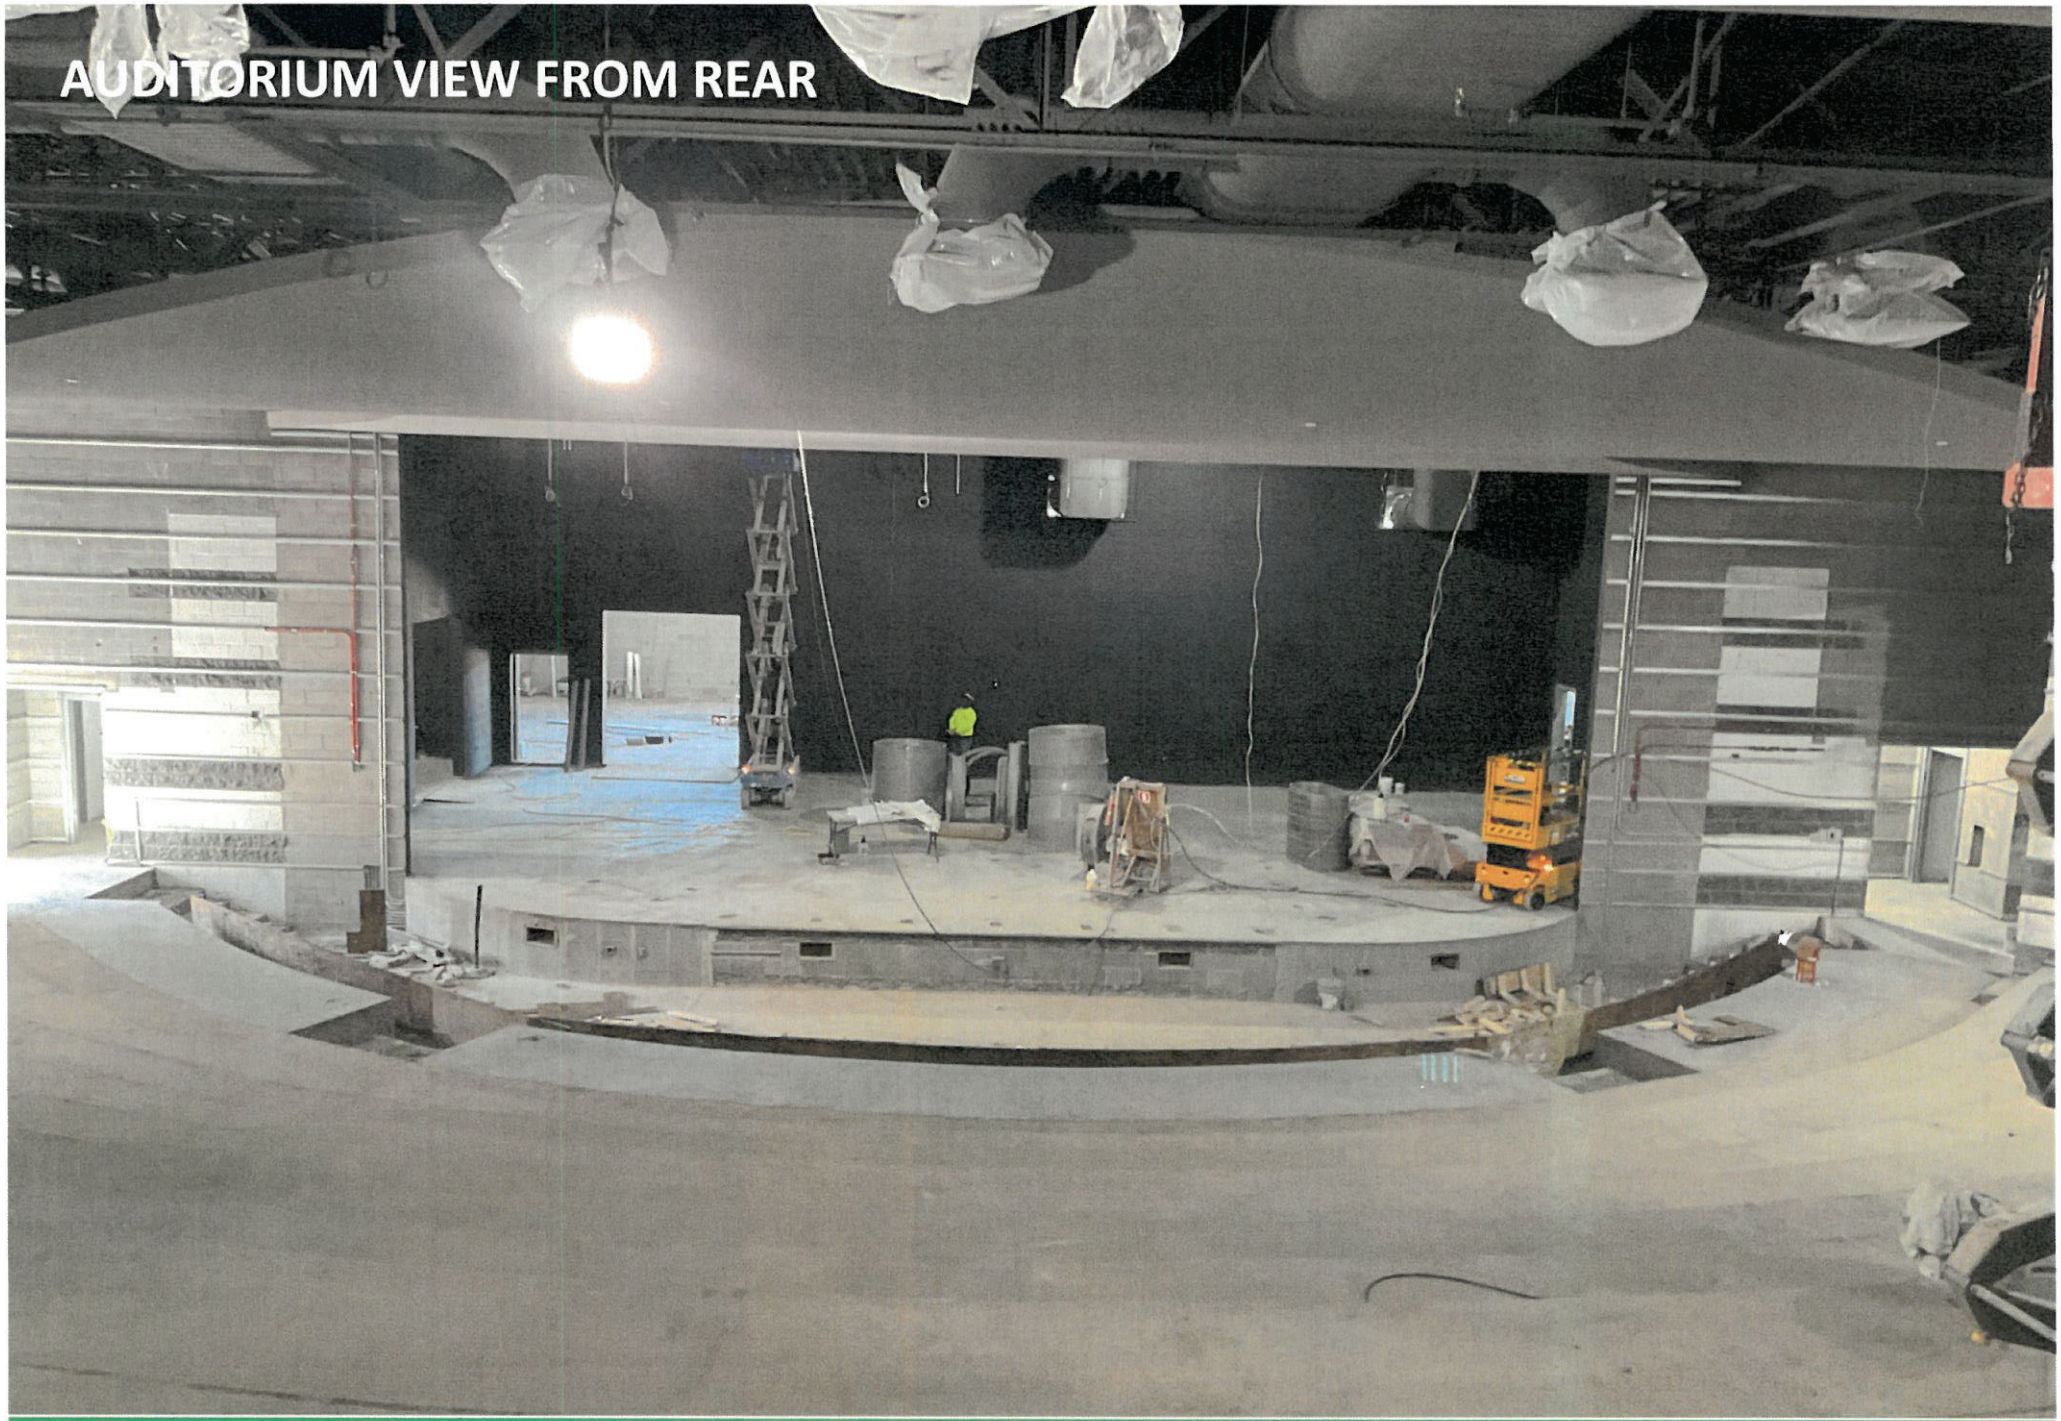
NAHS AUDITORIUM RENOVATION | NOVEMBER 2026

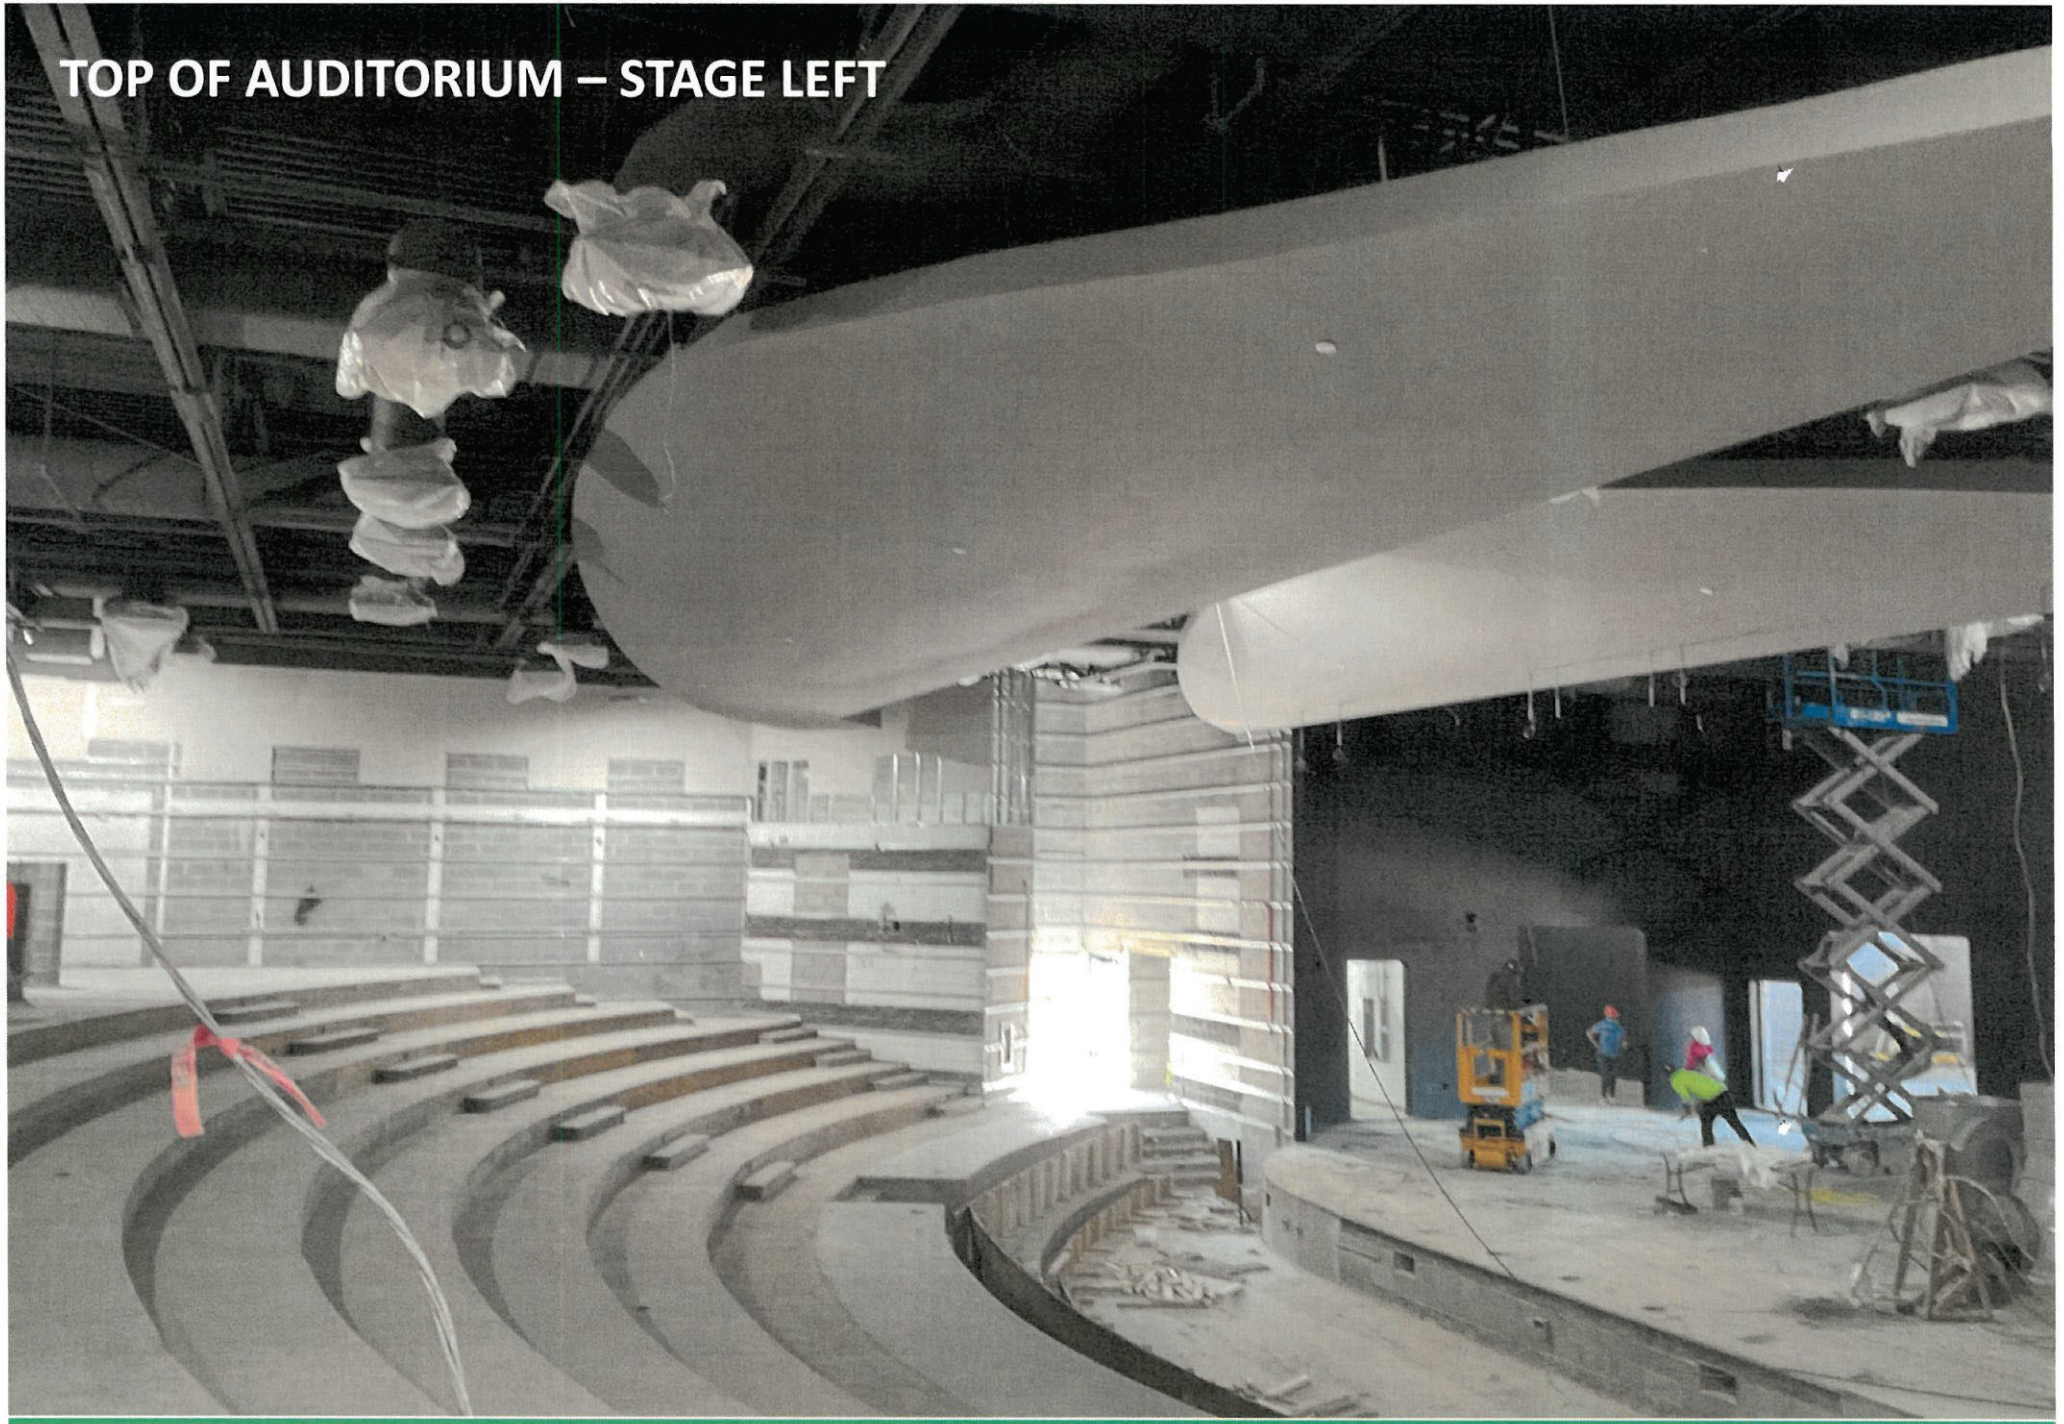
NEW ENTRANCE



AIKEN COUNTY PUBLIC SCHOOL DISTRICT

NAHS AUDITORIUM RENOVATION | NOVEMBER 2026


AUDITORIUM VIEW FROM REAR


TOP OF AUDITORIUM – STAGE LEFT

NORTH AUGUSTA HIGH SCHOOL
AUDITORIUM RENOVATION

PROJECT SCHEDULE:

- Estimated date of Final Completion: July 2027
- Project is on schedule.

PROJECT BUDGET:

- Original Contract Sum: $10,243,907.00
- Net Changes by COs: $0.00
- Contract Sum to Date: $10,243,907.00
- Amount Paid to Date: $5,117,579.37 (As of Oct. Pay App)

QUESTIONS & COMMENTS
